
Water Storage Investment Program Update



Estimated Timelines



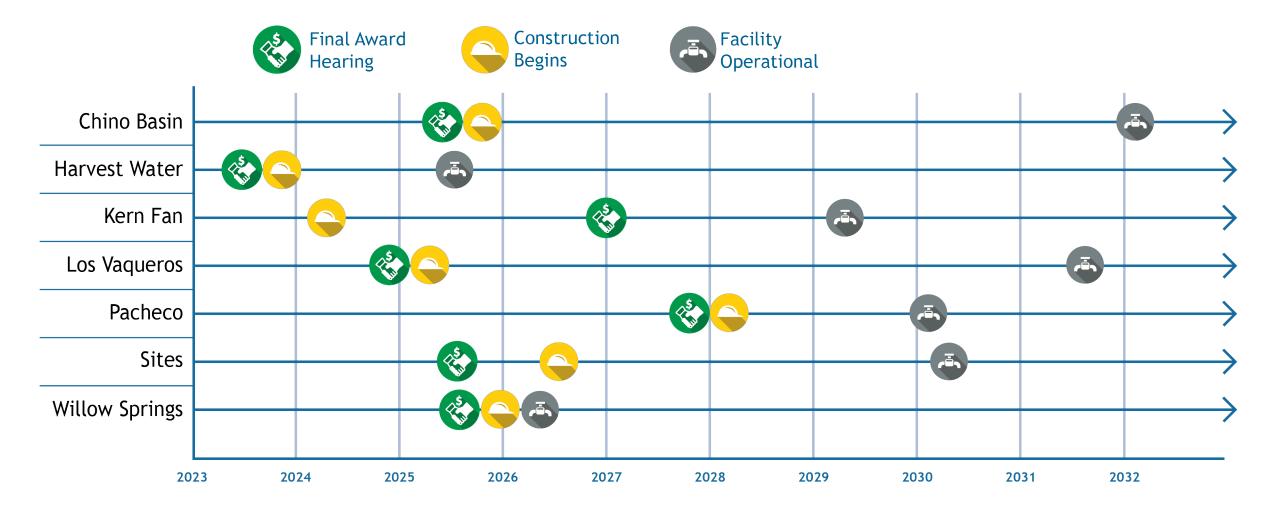

Harvest Water Program

Funding Recipient: SacSewer

Recent Activity	 Funding agreement executed Began construction activities Annual reports for public benefits contracts posted
Critical Next Steps/Milestones	Continue construction; begin invoicing
Estimated Final Award Date	Project received final award June 2023
Last Presentation to Commission	June 2023 final award hearing



Pacheco Expansion

Applicant: Valley Water

Recent Activity	Early funding expended, closing out agreement
Critical Next Steps/Milestones	 Draft Recirculated EIR/EIS release May 2025; Final August 2026 Permits September 2027 Public benefit contracts mid-2025; CWC staff estimate is 2027
Estimated Final Award Date	• 2027
Last Presentation Next Presentation	 April 2024 Recommend staff meet with Valley Water and report to Commission in July.

Los Vaqueros Expansion

Applicant: Contra Costa Water District

Recent Activity	Early funding expended, closing out agreement
Critical Next Steps/Milestones	 Applicant transfer to Los Vaqueros Joint Powers Authority (LVJPA) next quarter Record of Decision (ROD) September Draft public benefits contracts delayed from July 2024 to November 2024
Estimated Final Award Date	Shifted from Nov 2024 to June/July 2025
Last Presentation Next Presentation	 May 2022 additional early funding request November 2024 draft CAPBs

Chino Basin Program

Applicant: Inland Empire Utilities Agency (IEUA)

Recent Activity	 Early funding 83% expended Project cost estimate increased from \$650M to \$985M
Critical Next Steps/Milestones	 Completing preliminary design reports which will indicate permit pathway and schedule Exchange agreements with Metropolitan, DWR CAPB final draft date in quarterly report - unclear
Estimated Final Award Date	Mid- to late-2025
Last Presentation Next Presentation	 November 2023 increase in early funding Possibly early 2025

Willow Springs Water Bank

Applicant: Southern California Water Bank Authority

Recent Activity	 Early Funding: 38% expended; existing agreement expired. New early funding agreement work to start after existing agreement closed-out Draft EIR Pulse flow projects (incl. Chino and Kern Fan)
Critical Next Steps/Milestones	 Partnership agreement with AVEK: end of 2nd quarter 2024 Public benefits contracts August 2025
Estimated Final Award Date	October 2025
Last Presentation Next Presentation	 January 2024 project update Recommend September or November

Kern Fan Project

Applicant: Groundwater Banking Joint Powers Authority

Recent Activities	 Began construction of Phase 1 in early 2024 Cost estimate increased from \$171M to \$353M
Critical Next Steps/Milestones	 Turn-out location determined by end of 2024 Public benefit contracts August 2025 Permits late 2026
Estimated Final Award Date	• Early 2027
Last Presentation Next Presentation	April 2024None scheduled

Sites Reservoir

Applicant: Sites Reservoir Authority

Recent Activities	 Early funding expended, closing out agreement Water rights: protest resolution closed in March; hearing schedule released CEQA litigation ongoing
Critical Next Steps/Milestones	 Incidental Take Permits in October 2024 Public benefits contracts early 2025 Non-public benefit cost share September 2025
Estimated Final Award Date	Staff estimates late 2025
Last Presentation Next Presentation	May 2023 increase in early fundingNone scheduled
