



State Water Project Update on Key Issues

Carl A. Torgersen


Aug 2014

Key Items

1. Update on SWP operations
2. Update on Contract Extension
3. Update on Labor
4. Update of Fire Modernization
5. Significant Construction Projects
6. East Branch Extension Overview

East Branch Extension (EBX)

- A = Foothill Pipeline
- B = Santa Ana River Crossing (SARC) Pipeline
- C = Morton Canyon Connector
- D = Greenspot Pipeline
- E = Crafton Hills Pipeline
- F = Yucaipa Pipeline
- G = Bryant Pipeline
- H = Singleton Pipeline
- J = Noble Creek Pipeline
- K = Mentone Pipeline South
- L = Mentone Pipeline East

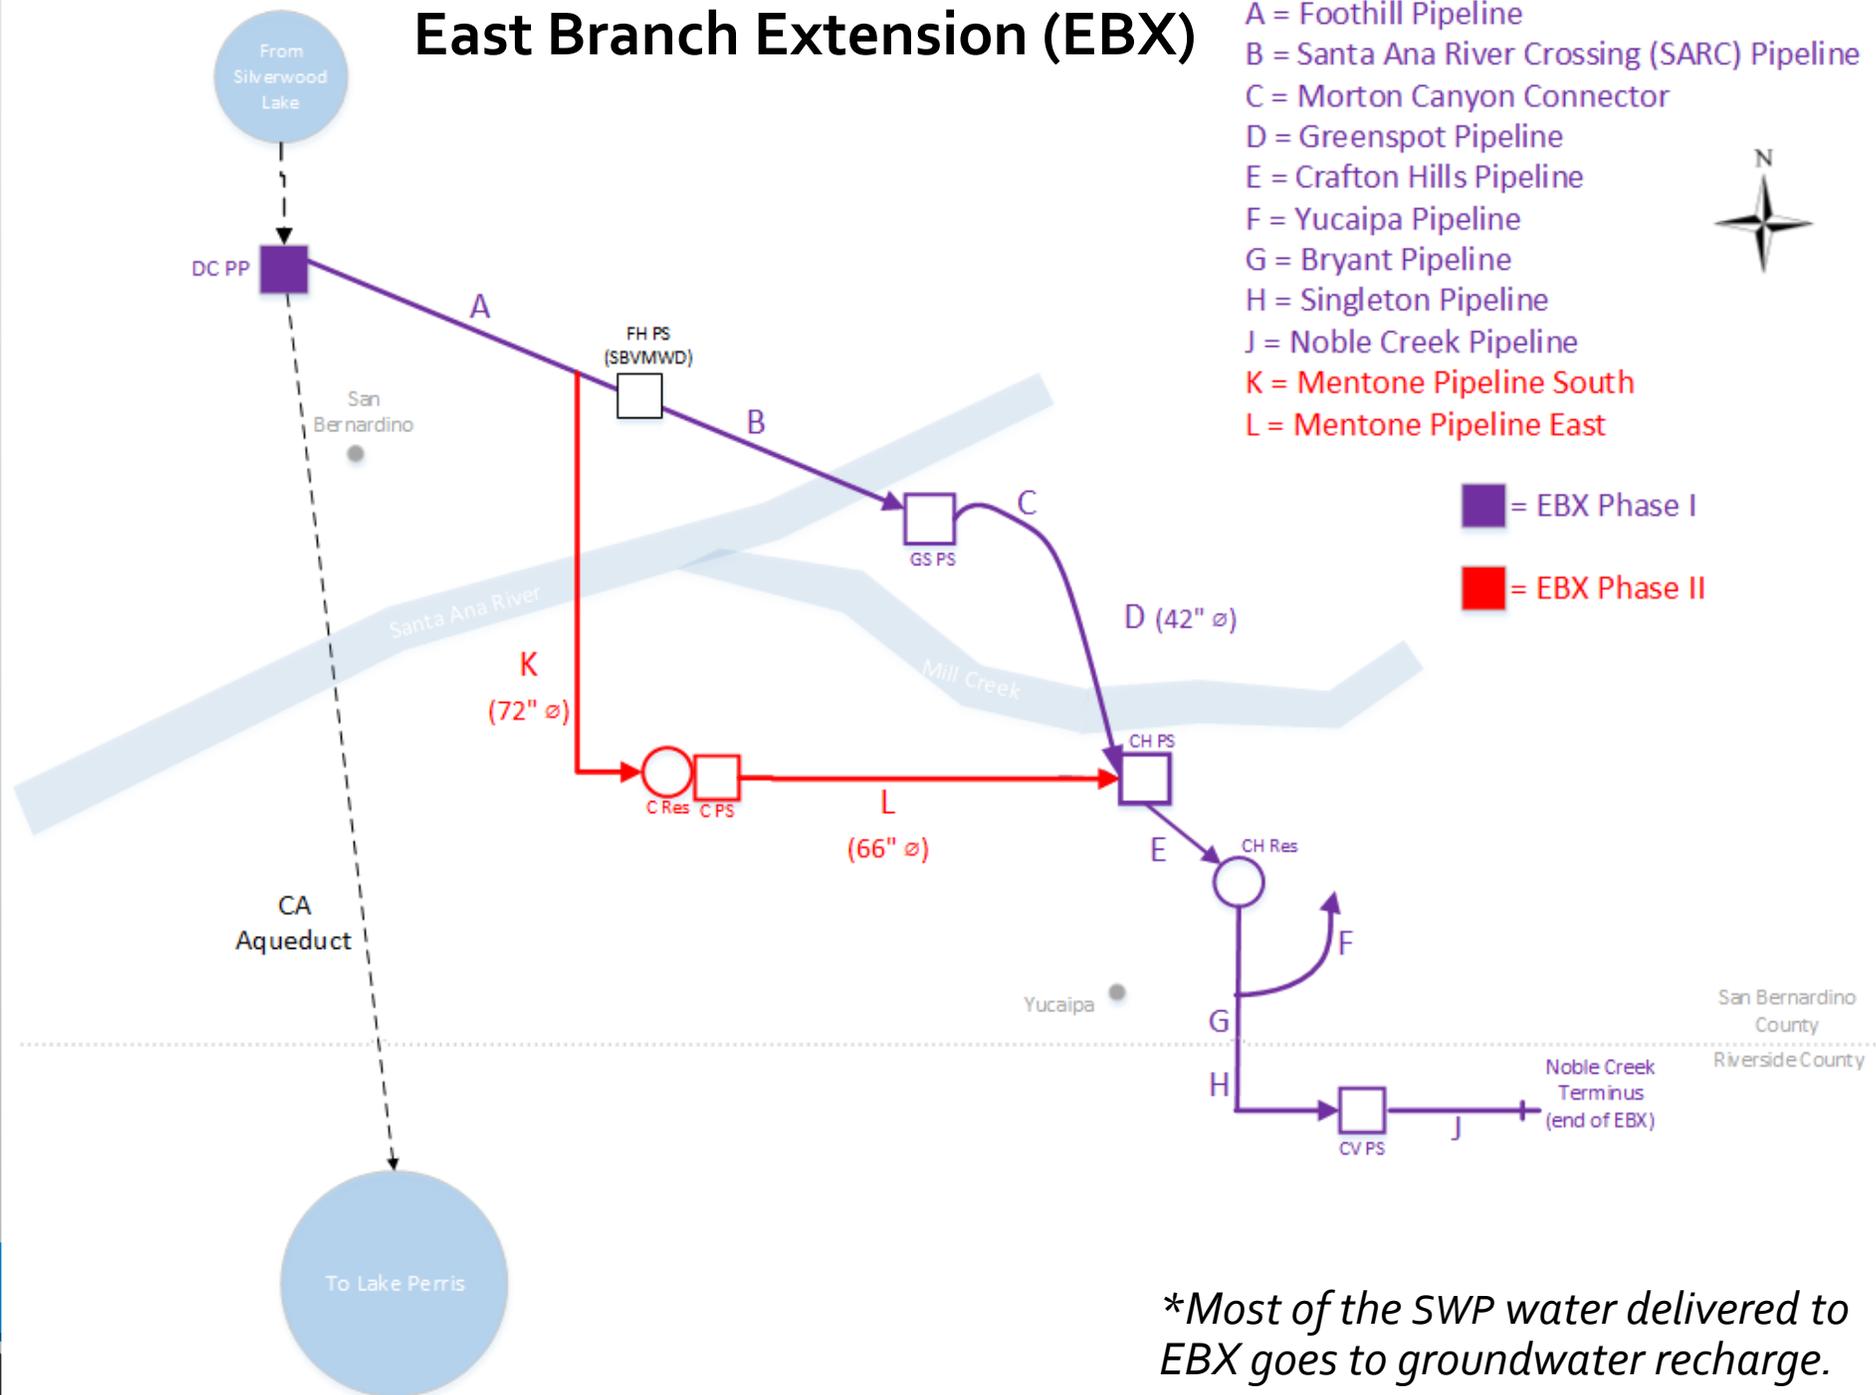

= EBX Phase I
 = EBX Phase II

**Most of the SWP water delivered to EBX goes to groundwater recharge.*

Timeline

- 1960 (Dec) – San Bernardino Valley MWD Contract Start Date
- 1962 (Nov) – San Gorgonio Pass WA Contract Start Date
- 1972 – San Bernardino received 1st SWP water delivery
- 1996 – EBX JPA w/ DWR, SGPWA, SBVMWD (**DWR to build EBX**)
- 2003 – EBX PI completed, San Gorgonio 1st water delivery
- 2005 – EBX PII begins
- 2009 – EBX PI Improvements begin
- 2016 (Jun) – EBX PI Improvements and EBX PII complete (projected)



Mentone Pipeline

Santa Ana River

Mentone Pipeline

Citrus Pump Station

Opal Ave

Citrus Reservoir

San Bernardino Avenue



Original Dam

Crafton Hills Reservoir

Expansion Dam





Crafton Hills Pump Station



Forebay Tank 2

Switchyard

Air Chamber



Forebay Tank 1

State Hwy 38

