

Water Storage Investment Program Quarterly Report

The quarterly reporting covered by this template documents an applicant's progress toward complying with [California Code of Regulations, title 23, section 6013\(d\)](#) in preparation for a final WSIP funding hearing with the Commission. This report also documents any changes to the physical quantity and type of public benefit being provided by the project. Commission staff relies on this report to keep the Commission informed of the project's progress, challenges and timeline. It is expected that each Applicant will be forthright and transparent in its reporting.

Applicants must provide an update of the project status for the requirements and milestones listed below. Applicants may deviate from this fill-in format, however, please provide the information requested in this template. Applicants must ensure this report is consistent with other publicly available project information, such as materials presented to the Applicant's governing body.

Project Information

Project name:

Kern Fan Project

Applicant name:

Groundwater Banking Joint Powers Authority (GBJPA)

Date:

July 30, 2026

Reporting period:

April 1, 2026 through June 30, 2026

Provide a brief project description:

The Kern Fan Groundwater Storage Project (Kern Fan Project) is a proposed conjunctive use project consisting of a regional water bank with a storage capacity of 100,000 acre-feet located in the Kern Sub-Unit of the San Joaquin Valley Groundwater Basin in Kern County, California. The Project would be constructed and owned by the Groundwater Banking Joint Powers Authority (GBJPA). The GBJPA is comprised of members Irvine Ranch Water District (IRWD) and Rosedale-Rio Bravo Water Storage District (Rosedale). The Kern Fan Project would capture, recharge and store wet-year surface water that would otherwise be lost to the ocean for water use as needed.

The Proposed project includes the construction of new recharge, recovery and conveyance facilities and will also utilize existing water bank facilities to maximize recharge during periods when Article 21 water is available. The Project includes construction of new recharge basins, up to 12 recovery wells, a modified turnout off the California Aqueduct, new conveyance canal and associated pipelines. The new conveyance

canal, referred to as the Joint Use Canal, will be constructed to deliver up to 375 cubic feet per second (cfs) of water. The Joint Use Canal will convey surface water to and from approximately 1,639 acres of land, which will consist of 991 acres of existing recharge basins owned by the Project sponsors and approximately 648 acres of new recharge basins.

- Phase 1: 350 acres of newly constructed recharge basins
- Phase 2: 991 acres of existing recharge basins
- Phase 2: 300 acres of new recharge basins that will be constructed

The 991 acres of existing recharge basins are underutilized and unable to recharge water during periods when Article 21 is available due to capacity limitations on existing regional conveyance.

Project storage capacity will be split between three storage accounts for Public and Non-Public Benefits. 25,000 AF will be allocated to an Ecosystem account, 37,500 AF to an IRWD account and the remaining 37,500 AF to a Rosedale account. IRWD and Rosedale have access to additional groundwater storage through Rosedale's existing Conjunctive Use Program. During periods when Article 21 water is available, but Project storage is full, IRWD and Rosedale can move their banked water to other storage accounts under the Conjunctive Use Program. The Project would be operated to store Article 21 water during wet years for the administration of Public and Non-Public Benefits. When Article 21 is not available, Project facilities would be used to recharge other sources of water including Section 215 water. During dry years, the stored water would be recovered for use.

Provide a brief description of public benefits:

Ecosystem Benefit- Fish Species Recovery: Approximately 25% of the Article 21 water stored by the Project would be dedicated for ecosystem benefits. The water would be used by DWR in an exchange that would provide short-term pulse flows to generate ecosystem benefits by improving habitat for fish species in the Feather and Sacramento Rivers and San Joaquin-Sacramento Delta.

Ecosystem Benefit- Incidental Wetland Habitat: The Central Valley is a crucial area along the Pacific Flyway for waterfowl. During recharge events, the inundated basins provide temporary habitat for waterfowl, shorebirds, raptors and other migratory birds.

Emergency Response Benefits- Extended Drought and Delta Failure: Groundwater stored as part of the project will be available to call on during a drought emergency or as an alternative supply in the case of a local supply outage. A separate emergency response benefit of the Project is the water supply provided by the Project in event of levee failure in the Delta that curtails water deliveries.

Water Supply Benefits: Water stored in the IRWD and Rosedale storage accounts would provide water supply benefits to IRWD, Rosedale and Dudley Ridge Water District. This water would be used for M&I and Agricultural purposes.

Increased Groundwater Level Benefit: The groundwater basin in Kern County is operated such that a portion of banked groundwater is not recovered by the banking entity and remains in the ground to bolster local groundwater levels. This "leave behind" water will improve water levels and provide a groundwater level benefit.

Agricultural Impact Benefit: An additional agricultural benefit from the Kern Fan Project is the preservation of permanent agricultural crops that would need to be replaced with low-value crops if the water from the Project were not available. The water stored by the Project would allow for preservation of approximately 1,600 acres of permanent crops in Kern County.

Current total project cost:

\$183 million capital cost (2025 dollars)

General Update and Key Issues

Provide a general update and describe any **key issues** that occurred during this reporting period. You may attach additional documents or pages if more space is needed:

During the current reporting period the GBJPA met with CDFW to discuss the Kern Fan Project operating model. Upon further review of the Kern Fan Project spreadsheet model, CDFW had questions related to the frequency of the Feather River pulse flows that can be facilitated by the Kern Fan Project during the first 50 years of the model simulation. The GBJPA and its modeling consultant, MBK Engineers, evaluated these uncertainties in the frequency of pulse flows under eight different hydrologic scenarios modeled with CalSim 3. On August 10, the GBJPA and MBK Engineers will present their modeling scenario recommendation for consideration by CDFW in preparation of the CAPB. Based on the selected hydrologic scenario, the GBJPA and MBK Engineers will summarize the modeled supplies that could be used in an emergency as part of the Emergency Response Benefit and schedule a follow up meeting with DWR to resume discussions on the CAPB for emergency water supply benefits.

IRWD and Rosedale met with the Kern County Water Agency and Dudley Ridge Water District to discuss next steps in advancing discussions with DWR on implementing pulse flow exchanges for the Project. IRWD also met with Metropolitan Water District to discuss their potential participation in the Kern Fan Project through facilitating operational exchanges in the California Aqueduct.

During the current reporting period, a draft Joint Use Canal Alternative 5 (Alt-5) Feasibility Report for the turnout and conveyance facilities from the California Aqueduct was completed. The Feasibility Report evaluated four alternatives for conveyance from the California Aqueduct to the Project using the existing Cross Valley Canal (CVC) turnout with improvements to the turnout and CVC pools. The preliminary preferred option consists of a single 1,650 cfs canal for the first four miles of the CVC with liner raises in subsequent sections of the canal. A new pump station and a two-mile pipeline would be constructed to deliver water to Kern Fan Project recharge facilities. IRWD and Rosedale staff reviewed the Feasibility Report and presented the report findings at the GBJPA Board meeting on June 17. Following the Board meeting, a separate workshop was held to present the Feasibility Report to stakeholders. During the next reporting period, the GBJPA plans to present the Feasibility Report to the CVC Advisory Committee and seek a decision on which Alternative identified in the Report to pursue.

During the reporting period, construction continued on the Phase 1 recovery facilities. The construction contractor continued work on the four well sites and installed underground electrical conduits, grounding, and formwork, reinforcement steel, and concrete placement for well foundations and electrical pads.

Attach latest project schedule. In addition, describe below how the actual schedule is progressing in comparison to the schedule provided in the last reported schedule:

Attached as Exhibit "A" is the Funding Agreement Milestone Schedule entitled "Project Schedule (CWC Table 1)". The schedule provides the milestones stipulated in the Maximum Conditional Eligibility Determination Letter dated July 27, 2018.

Attached as Exhibit "B" is an updated Kern Fan Project overall schedule, which includes the Commission requirements, as well as planning and project studies, environmental documentation, design, and construction. Tasks under "Right-of-Way & Easements" were streamlined; the completion dates for executed easements & rights-of-way have not changed.

Note any milestones or accomplishments that occurred since submitting the prior Quarterly Report:

In May the GBJPA closed escrow on 242 acres of land that will be the location for Phase 2 recharge and recovery facilities. Design of Phase 2 facilities is currently underway.

The GBJPA also executed the Early Funding Agreement with the CWC and is preparing the first invoice which will be submitted during the next reporting period.

Provide an update on Tribal consultation, and Tribal and community engagement, if any. Please note any ongoing issues with Tribal communities, including differences of opinion or opportunities to work together:

N/A

Items Required Prior to Scheduling a Final Award Hearing

Provide the date (month/year) that you expect to request a Final Award Hearing from the Commission. Note: the request should be received at least 2 months before the anticipated Final Award Hearing date and after all items required by California Water Code section 79755 are completed:

January 2028

Provide the date (month/year) that you anticipate a Final Award Hearing with the Commission:

March 2028

The following items must be provided prior to scheduling a final award hearing. Please describe the status and include the estimated completion date for the following items. These dates should align with any attached project schedule:

1. Contracts for non-public benefit cost share:

List all required contracts for non-public benefit cost share, and provide the amount of associated funds, the status and estimated completion date. Please note any issues or concerns that have, will, or could affect the timing of executing contracts for non-public benefit cost share.

Contract Name	\$ Amount	Status	Est
---------------	-----------	--------	-----

			Completion Date
GBJPA Agreement	\$233.6 million (estimated)	The Groundwater Banking Authority JPA agreement executed in 2020 includes a provision that IRWD and Rosedale will each fund 50% of the non-grant funded project cost. No contracts, other than the executed Joint Powers Authority Agreement between Rosedale and IRWD, are anticipated. A funding commitment letter to the Director of the Department for the non-public benefits was submitted in October 2021. The current estimated project cost is \$353.75 million in 2024 dollars. The Kern Fan Project has been awarded approximately \$120.1 million in grant funding. The GBJPA will fund the remaining cost of the Project.	October 2021

2. Contracts for administration of public benefits (CAPB):

Provide an estimated date when all Draft CAPBs will be complete. The Draft CAPB completion date is when the agreement is ready and available to post for public review at a subsequent Commission meeting:

In August 2023, the GBJPA met with CDFW to discuss development of the CAPB agreement. At that time, CDFW staff recommended that work on the CAPB agreement be deferred until the location of the Aqueduct turnout has been finalized with updated modeling of pulse flows. The GBJPA is currently engaged in discussions with CDFW and DWR on the CAPBs. At this time, the GBJPA estimates that the draft CAPBs will be available by September 2027.

Provide a status for each applicable administering agency's Draft CAPB. Please note any issues or concerns that have, will, or could affect the timing of the Draft CAPBs:

	Status
Draft CAPB	In August 2025, the Kern Fan Project proponents met with CDFW to discuss ecosystem benefits provided by the project and next steps for the development of the draft CAPB. In February 2026, the GBJPA met with its modeling consultant and CDFW to review the Kern Fan Project model and answer CDFW's questions. During the current reporting period, the GBJPA and its modeling consultant evaluated uncertainties in the frequency of Feather River pulse flows that can be facilitated by the Kern Fan Project under eight different hydrologic scenarios modeled with Calsim 3. During the next reporting period the GBJPA will meet with CDFW and discuss a final recommended modeling scenario for use by CDFW and DWR in the preparation of the CAPBs.

Provide an estimated date when all Final CAPBs will be complete. The Final CAPB completion date is when it will be executed:

December 31, 2027

Provide a status for each applicable administering agency's Final CAPB. Please note any issues or concerns that have, will, or could affect the timing of executing CAPBs:

	Status
--	---------------

Final CAPB	Discussions with DWR and CDFW for the CAPB are ongoing. The GBJPA expects to make a final determination of the appropriate modeling scenario to utilize during the next reporting period.
-------------------	---

List all public benefits, including quantity of benefit (e.g., acres of habitat, acre-feet of water for pulse flows, etc.):

Benefits	Description and Quantity of Benefits
Ecosystem Benefit – Fish Species Recovery	Approximately 25% of the Article 21 water stored by the Project would be dedicated for ecosystem benefits. The water would be used by DWR in an exchange that would provide short-term pulse flows to generate ecosystem benefits by improving habitat for fish species in the Feather and Sacramento Rivers and San Joaquin-Sacramento Delta.
Ecosystem Benefit – Incidental Wetland Habitat	The Central Valley is a crucial area along the Pacific Flyway for waterfowl. During recharge events, the inundated basins provide temporary habitat for waterfowl, shorebirds, raptors and other migratory birds.
Emergency Response Benefits – Extended Drought and Delta Failure	Groundwater stored as part of the project will be available to call on during a drought emergency or as an alternative supply in the case of a local supply outage. A separate emergency response benefit of the Project is the water supply provided by the Project in event of levee failure in the Delta that curtails water deliveries.
Water Supply Benefits	Water stored in the IRWD and Rosedale storage accounts would be water supply benefits to IRWD Rosedale and Dudley Ridge Water District. This water would be used for M&I and Agricultural purposes.
Increased Groundwater Level Benefit	The groundwater basin in Kern County is operated such that a portion of banked groundwater is not recovered by the banking entity and remains in the ground to bolster local groundwater levels. This "leave behind" water will improve water levels and provide a groundwater level benefit.
Agricultural Impact Benefit	An additional agricultural benefit from the Kern Fan Project is the preservation of permanent agricultural crops that would need to be replaced with low-value crops if the water from the Project were not available. The water supplies stored by the Project would allow for preservation of approximately 1,600 acres of permanent crops in Kern County.

Indicate if there are any anticipated changes to the benefit or quantity of the benefit since the original application and whether these changes affect the cost allocation:

The Kern Fan Project benefits have been updated based on the design changes to the Project, The GBJPA estimates that the Project will provide \$202.5 million in Public Benefits. The GBJPA will work with CWC staff to finalize the quantification of the benefits prior to the Final Award Hearing.

3. Completed feasibility studies:

Completion Date:

November 22, 2021

4. Complete environmental documentation:

Provide the status and estimated completion date for all required environmental documentation (draft and final) for the project, including all Board resolutions adopting or certifying CEQA environmental documents,

CEQA findings, mitigation monitoring and reporting program, Notice of Determination (NOD), and CEQA Addenda, and all NEPA completion documents, including the Record of Decision (ROD). Please note any issues or concerns that have, will, or could affect the timing of providing complete environmental documentation at the state or federal level.

Environmental Document	Status	Est Completion Date
State Document	Draft:	
	Final: Kern Fan Groundwater Storage Project Final EIR	12/20/2020
	NOD: Kern Fan Groundwater Storage Project Final EIR	1/22/2021
	Pulse Flow Component of WSIP Groundwater Projects SEIR	5/20/2024
	Kern Fan Groundwater Storage Project Supplemental EIR (Turnout/Conveyance)	4/1/2027
Federal Document	Draft:	
	Final: Phase 1 No Effect Determination	5/20/2024
	ROD	

5. All required federal, state, and local approvals, certifications, and agreements:

List permits needed for project to begin construction, describe status in acquiring them, and include estimated date to be acquired. Please note any issues or concerns that have, will, or could affect the timing of acquiring all federal, state, and local approvals, certifications, agreements, and permits necessary to begin project construction.

Approvals / Certifications / Agreements / Permits	Status	Est Date Acquired
Permits	Provided as Exhibit C Completion dates for the CalTrans Stockdale Hwy Crossing permit and Kern County Environmental Health Department Well Drilling Permits have been modified and are consistent with modifications made to Exhibits "A" and "B".	
Right of Way and Easements	Provided as Exhibit C	
Agreements	Provided as Exhibit C The completion dates for the required agreements have been modified and are consistent with modifications made to Exhibits "A" and "B"	

Items Required to Execute a Funding Agreement

Provide an update on the following documents needed to execute a funding agreement for the project and indicate if any significant change has occurred. The Commission may request updated information prior to executing a funding agreement.

	Status	Significant Change?
Applicant's audited financial statements	Audited financial statements are available and will be submitted prior to the funding agreement hearing.	No
Final project costs, schedule, and scope of work	The most recent Project cost and scope of work is available in the Feasibility Study submitted to the CWC November 2021. Updated Project schedules are provided as Attachments A and B. Final project costs, scope of work, and schedule will be provided to the CWC prior to the funding agreement hearing. The Kern Fan Project capital cost was updated based on the design changes and is estimated to be \$183 million in 2025 dollars.	No
Evidence of bilateral communications with operators and owners of potentially impacted facilities regarding potential impacts of the proposed project to their facilities	n/a	n/a
Limited waiver of sovereign immunity	n/a	n/a

Status Update

Provide a status update for the following and indicate if any significant change has occurred. The Commission may request updated information prior to executing a funding agreement.

	Status	Significant Change?
Labor Compliance	n/a	n/a
Urban Water Management Plans	IRWD is an urban water supplier and is required to submit an Urban Water Management Plan. IRWD adopted its 2025 Urban Water Management Plan and submitted it to DWR on June 29, 2026.	Yes
Agricultural Water Management Plans	Rosedale is an independent special district under the provisions of the California Water Storage District Law and therefore is not required to complete an Agricultural or Urban Water Management Plan.	n/a
Potential effect of other conditional	A Supplemental Environmental Impact Report for proposed pulse flow benefits provided by the Kern Fan Project, Willow Springs Water Bank and Chino Basin	No

eligible projects on the applicant's public benefits	Program has been released. A Final SEIR was completed and certified by DWR in July 2024.	
--	--	--

Other Pertinent Information:

1. Sources of Funding

List sources of funding (e.g., Federal, State grants, local partnerships, rate payers, loans...) to move the project to construction and provide the associated amount of funds from that source and a status of obtaining that funding source below:

Funding Sources	\$ Amount	Status	Est Award Date
GBJPA	\$233.6 million	Under the GBJPA, both IRWD and Rosedale will fund the Project. IRWD and Rosedale have established funding plans for their share of Project costs. The GBJPA will update its cost share based on updated operations, maintenance, and replacement costs in the next quarter.	Completed
State of California	\$111.4 million	The GBJPA expects to have a Funding Agreement with the CWC in early 2028. In August 2025, the California Water Commission voted to provide a \$22.3 million increase in conditional funding for the Kern Fan Project to offset inflationary cost impacts.	Mar-2028
Bureau of Reclamation	\$8.7 million	IRWD has an executed funding agreement with the Bureau of Reclamation for \$8.7 million for work on Phase 1 of the Project.	May-2024

2. Early Funding Agreement Status

Provide the status of the Early Funding Agreement (EFA), as applicable, and the percentage of EFA funds expended. If the EFA has been closed, describe how the remaining work needed to move the project to a final award hearing will be financed.

Status	Percentage of EFA funds expended
The GBJPA's early funding request was approved by the CWC at the January 21, 2026 meeting. The GBJPA adopted a resolution in February for the authorization to enter into an agreement with CWC to accept early funding for the Kern Fan Project. In May 2026, the GBJPA executed the Early Funding Agreement with the CWC. The GBJPA is preparing the first invoice and expects to submit the invoice to	0%

the CWC in the next reporting period.	
---------------------------------------	--


EXHIBIT "A" Project Schedule (CWC Table 1)
--

ID	Task Mode	Task Name	Duration	Start	Finish	Timeline																											
						2018 H2	2018 H1	2019 H2	2019 H1	2020 H2	2020 H1	2021 H2	2021 H1	2022 H2	2022 H1	2023 H2	2023 H1	2024 H2	2024 H1	2025 H2	2025 H1	2026 H2	2026 H1	2027 H2	2027 H1	2028 H2	2028 H1	2029 H2	2029 H1	2030 H2	2030 H1	2031 H2	2031 H1
0		Kern Fan Groundwater Storage Project	3218 days	Mon 9/3/18	Tue 12/31/30	Kern Fan Groundwater Storage Project																											
1		Contracts for Non-Public Benefits Cost Share	478 days	Mon 9/3/18	Wed 7/1/20	Contracts for Non-Public Benefits Cost Share																											
2		Execution of JPA Agreement for Kern Fan Project Authority	174 days	Fri 11/1/19	Wed 7/1/20	Execution of JPA Agreement for Kern Fan Project Authority																											
3		Executed Non-Public Benefit Cost Share Contracts to Commission	1 day	Wed 7/1/20	Wed 7/1/20	Executed Non-Public Benefit Cost Share Contracts to Commission																											
4		Contracts for Administration of Public Benefits	610 days	Mon 9/1/25	Fri 12/31/27																												
5		DWR Draft CAPB	545 days	Mon 9/1/25	Fri 10/1/27	DWR Draft CAPB																											
6		CDFW Draft CAPB	545 days	Mon 9/1/25	Fri 10/1/27	CDFW Draft CAPB																											
7		CWC Review of CAPB	65 days	Mon 10/4/27	Fri 12/31/27	CWC Review of CAPB																											
8		Completed Feasibility Study	534 days	Mon 12/2/19	Wed 12/15/21	Completed Feasibility Study																											
9		Preparation of Draft Feasibility Study	459 days	Mon 12/2/19	Wed 9/1/21	Preparation of Draft Feasibility Study																											
10		Draft Final Feasibility Study to Commission	59 days	Wed 9/1/21	Mon 11/22/21	Draft Final Feasibility Study to Commission																											
11		Final Feasibility Study to Commission	18 days	Mon 11/22/21	Wed 12/15/21	Final Feasibility Study to Commission																											
12		Environmental Documentation	1980 days	Mon 9/2/19	Thu 4/1/27	Environmental Documentation																											
13		Preparation of CEQA+ (Supplemental EIR-NEPA Compliant)	370 days	Mon 9/2/19	Fri 1/29/21	Preparation of CEQA+ (Supplemental EIR-NEPA Compliant)																											
14		Submittal of Public Review Draft CEQA to Commission	24 days	Tue 9/29/20	Fri 10/30/20	Submittal of Public Review Draft CEQA to Commission																											
15		Submittal of Final CEQA Document to Commission	0 days	Mon 7/27/20	Mon 7/27/20	Submittal of Final CEQA Document to Commission																											
16		Supplemental EIR for Pulse Flow Projects	675 days	Tue 3/1/22	Mon 9/30/24	Supplemental EIR for Pulse Flow Projects																											
17		CEQA for Turnout and Conveyance	400 days	Fri 9/19/25	Thu 4/1/27	CEQA for Turnout and Conveyance																											


Project: Kern Fan Groundwater


Date: Tue 7/21/26


Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

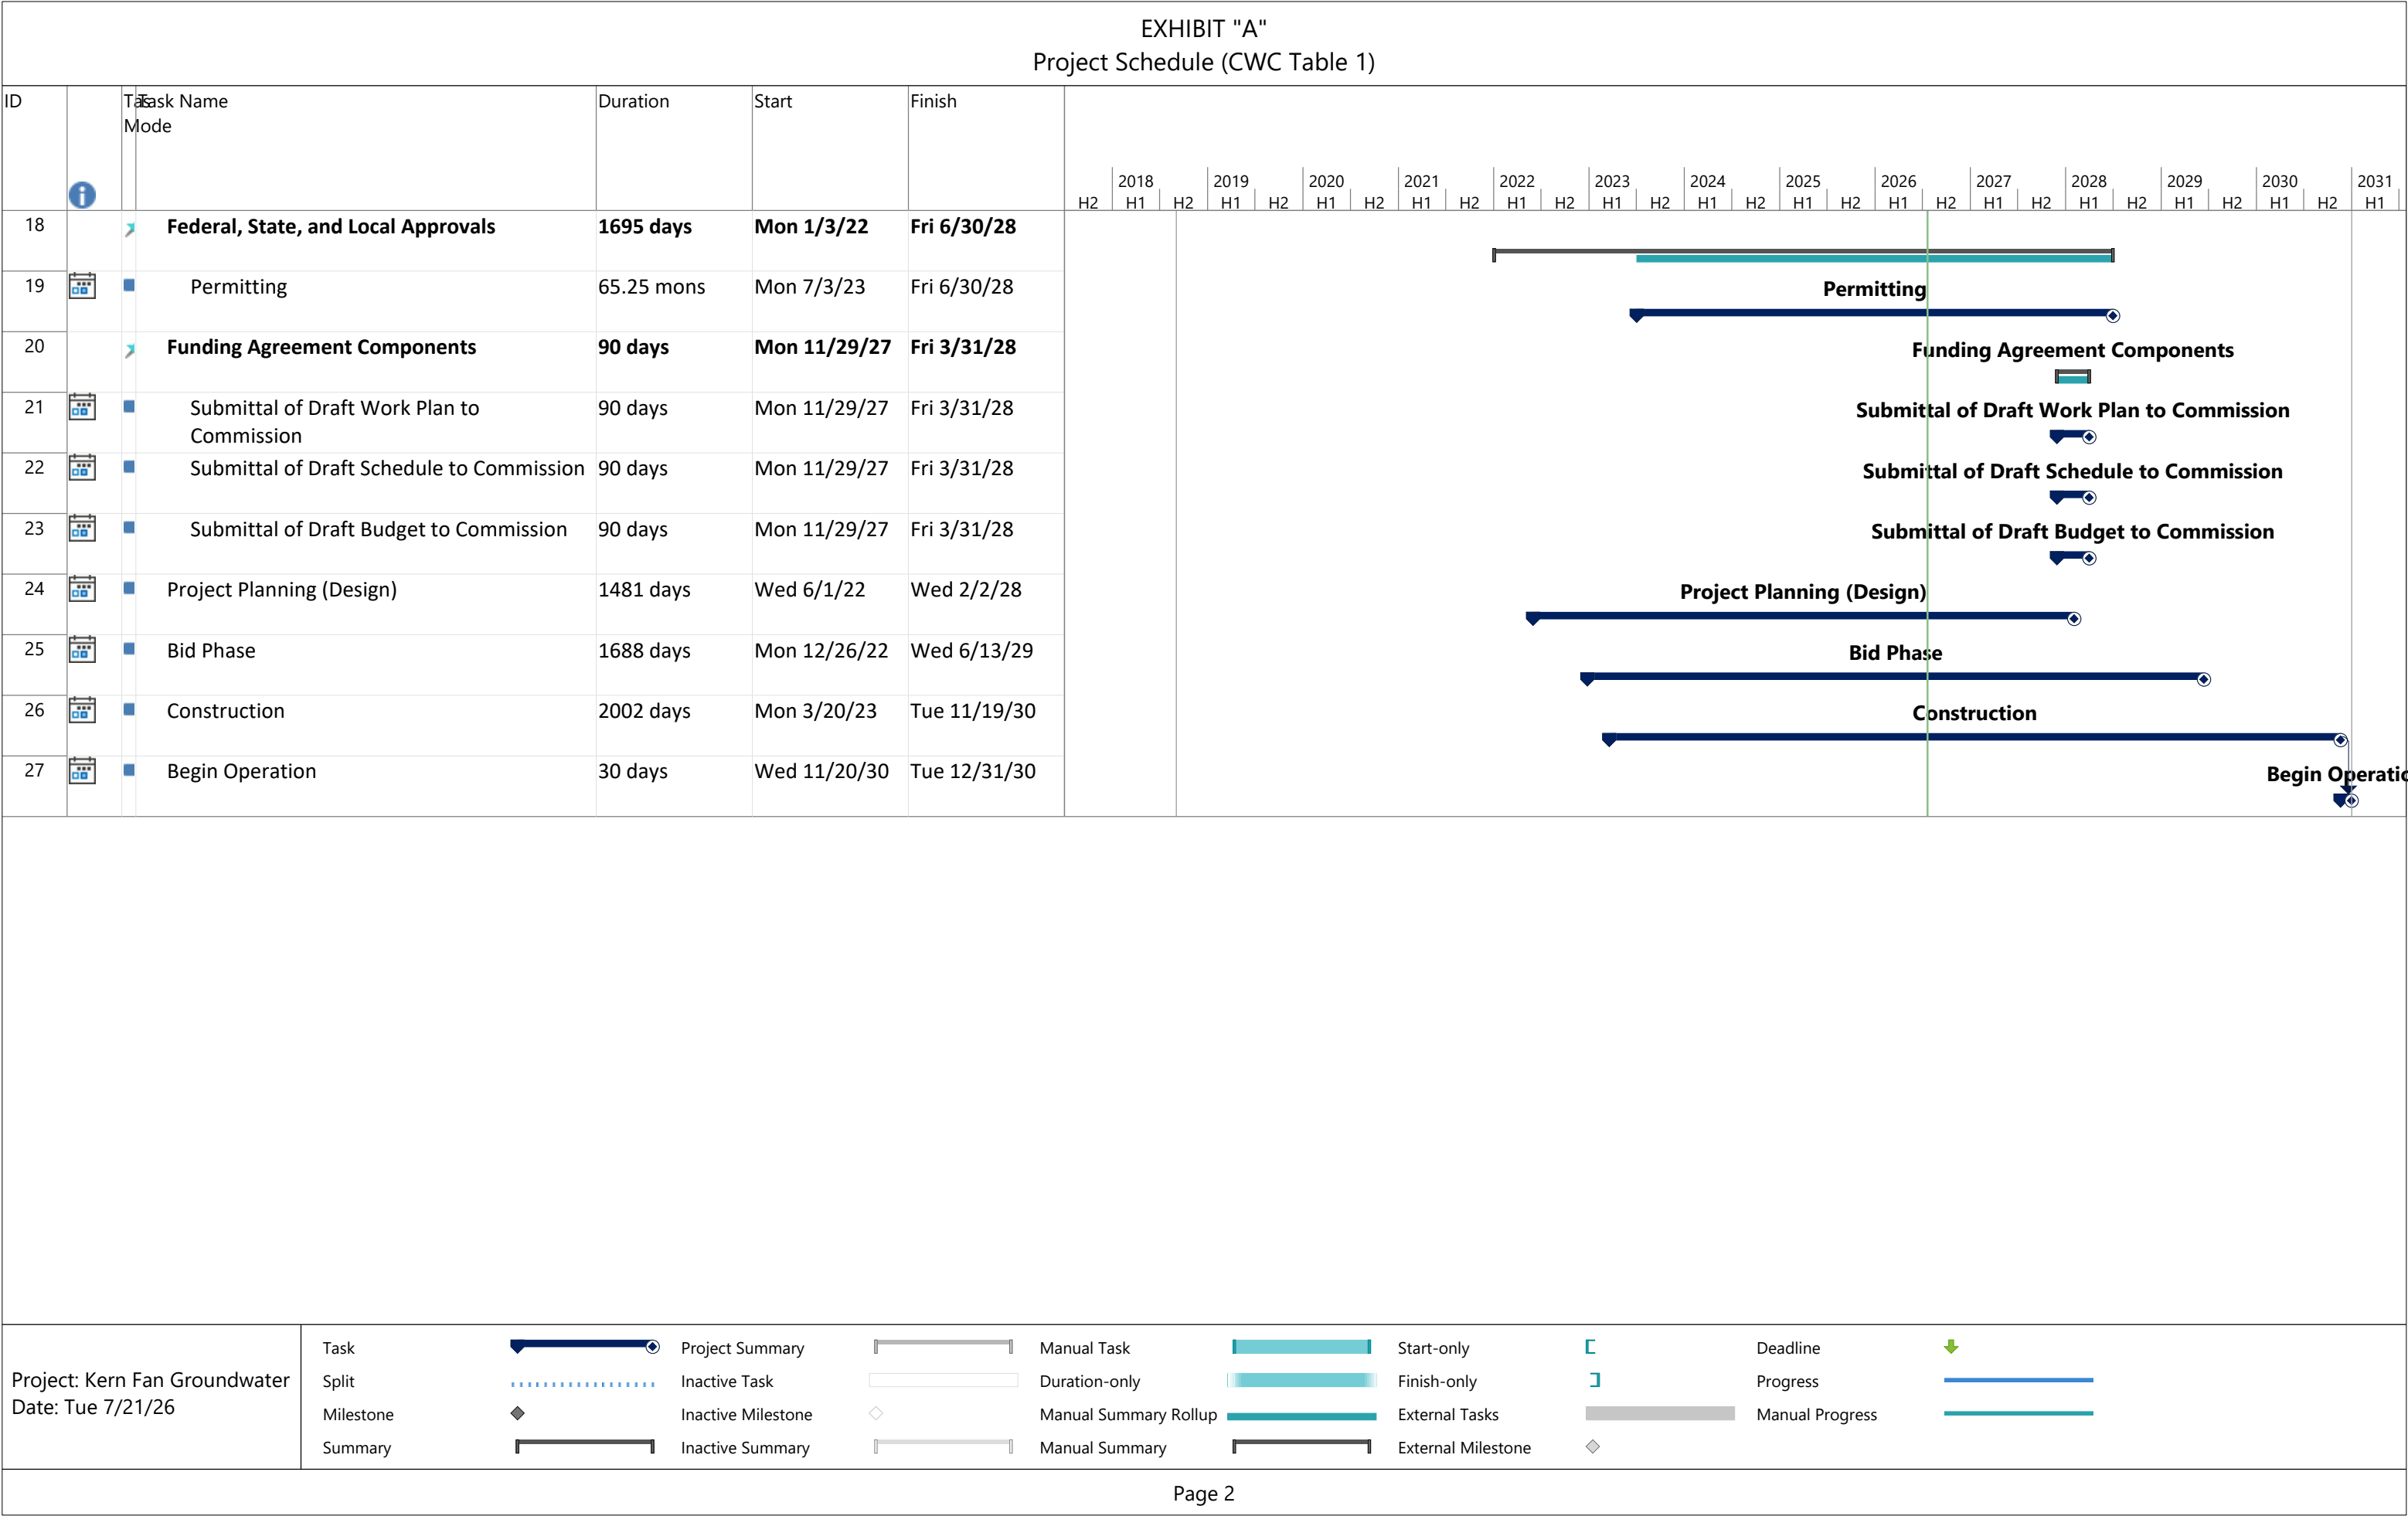

Page 2

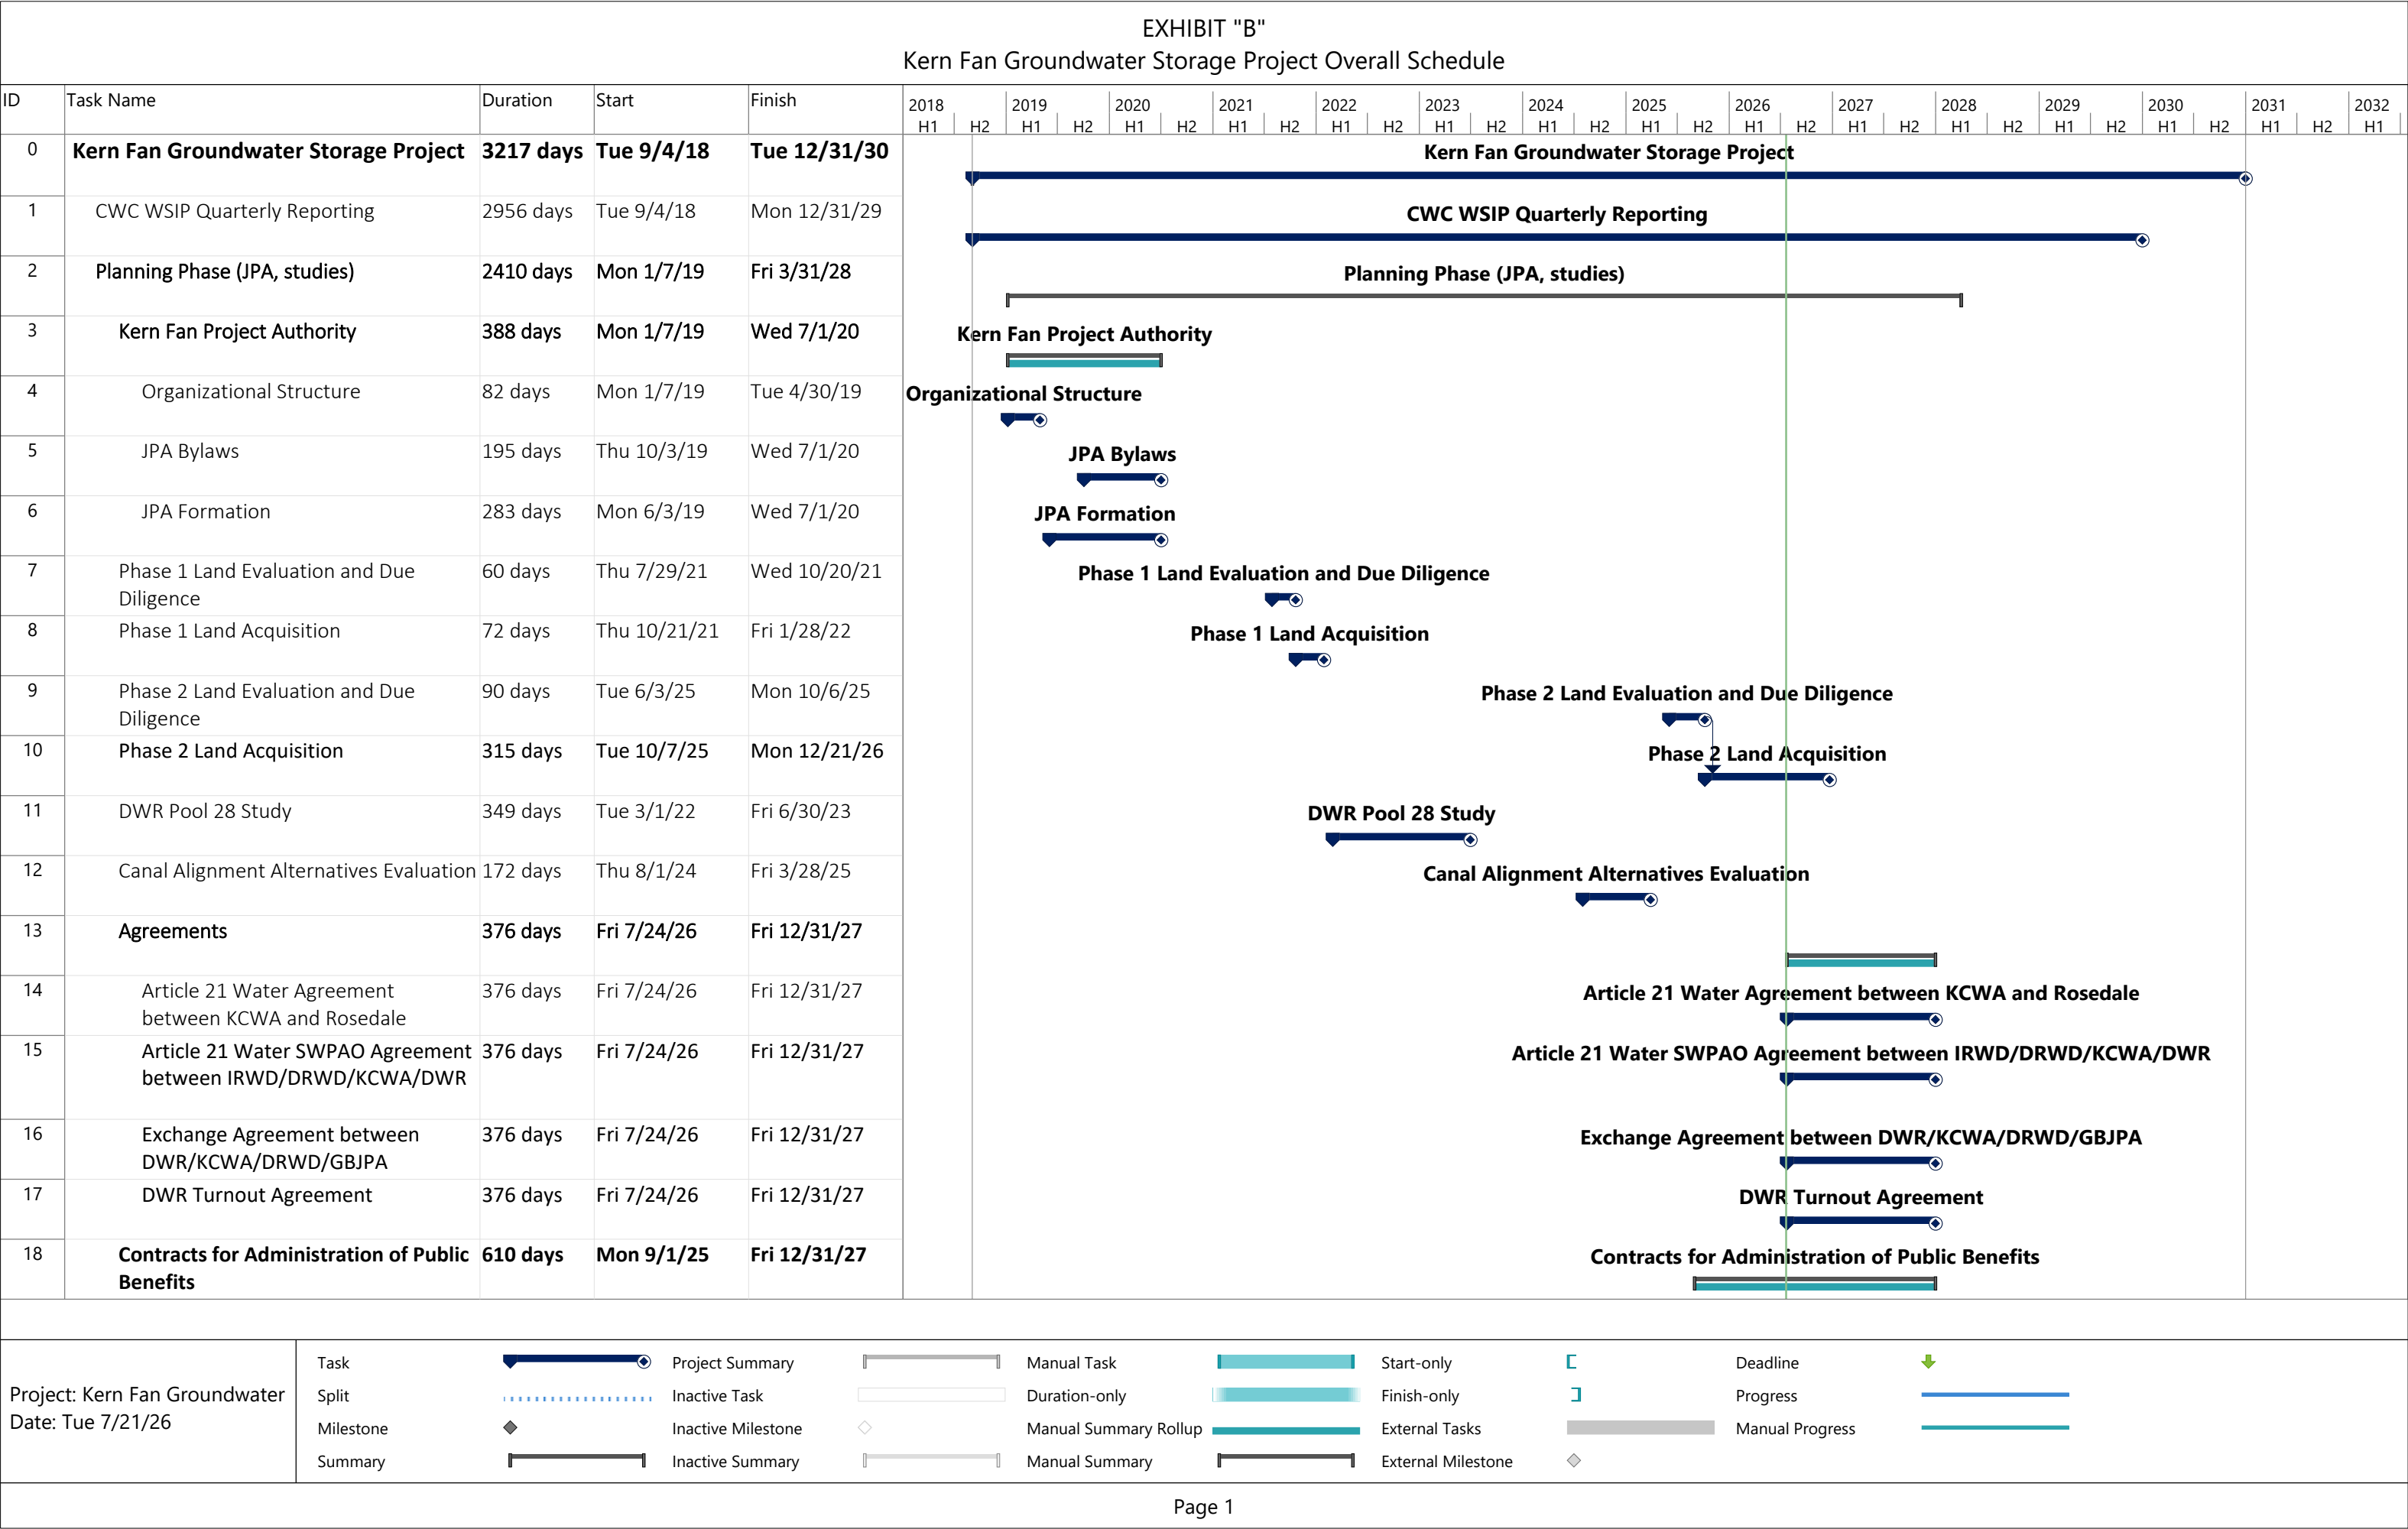

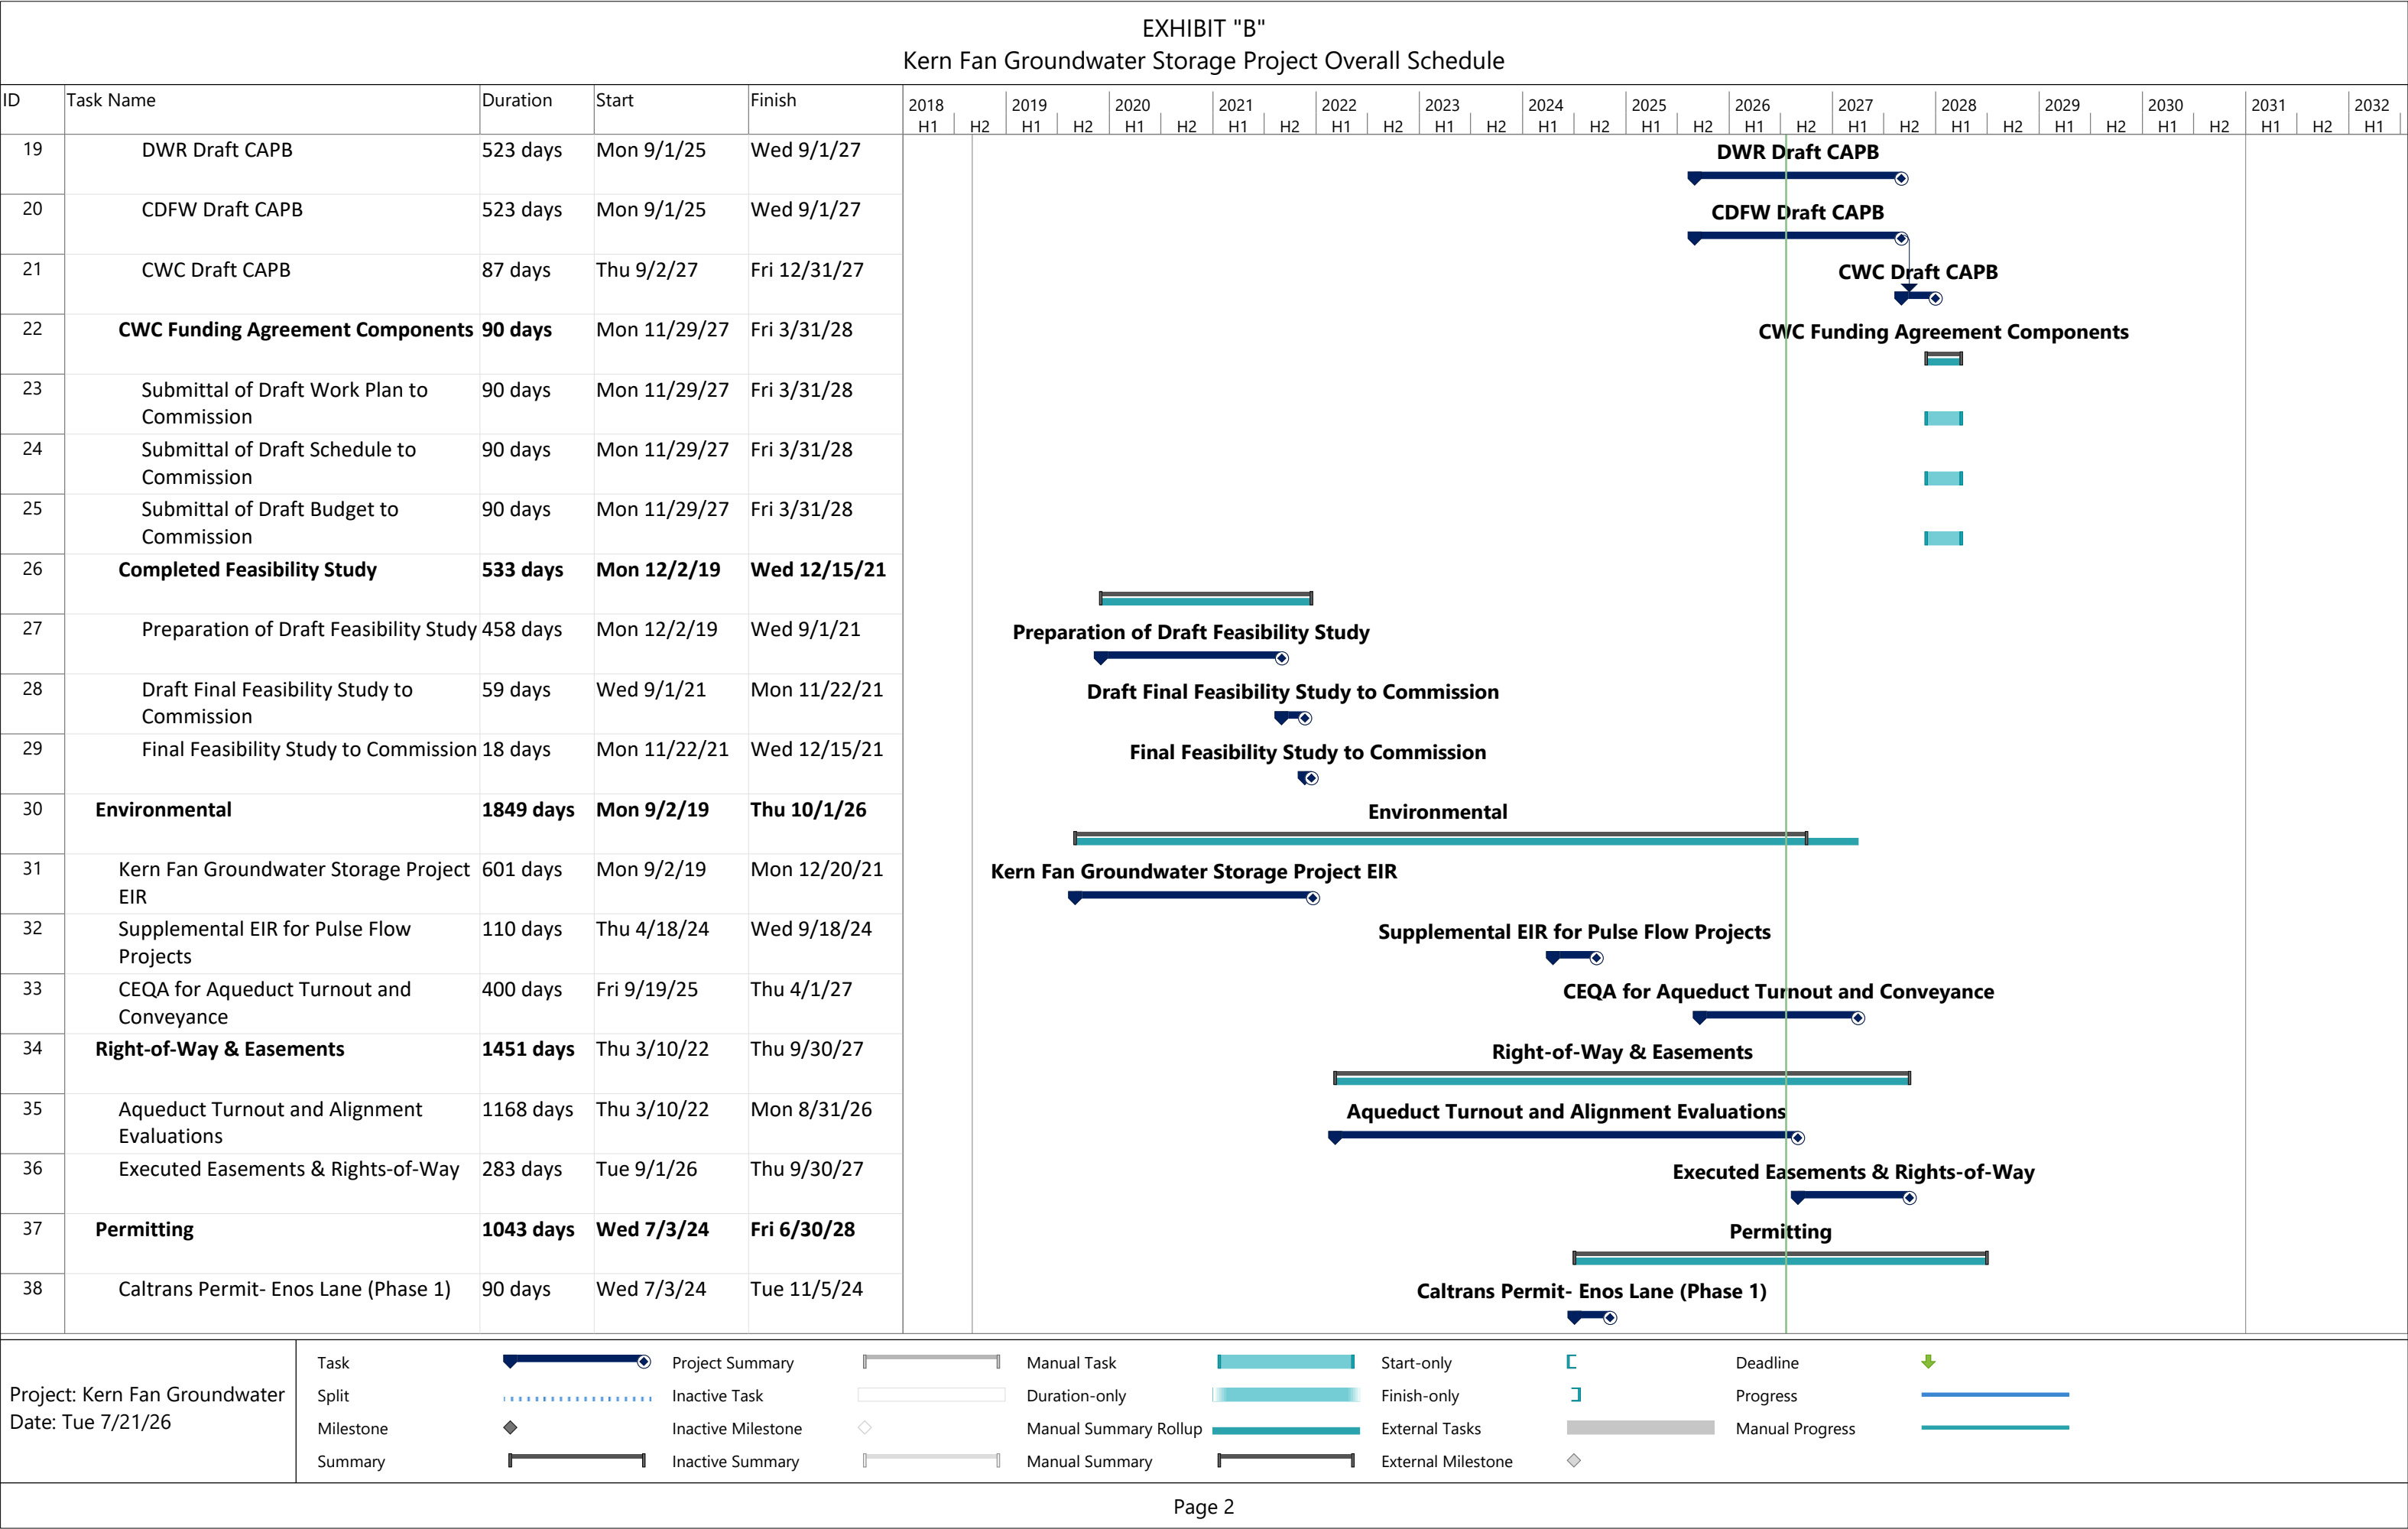

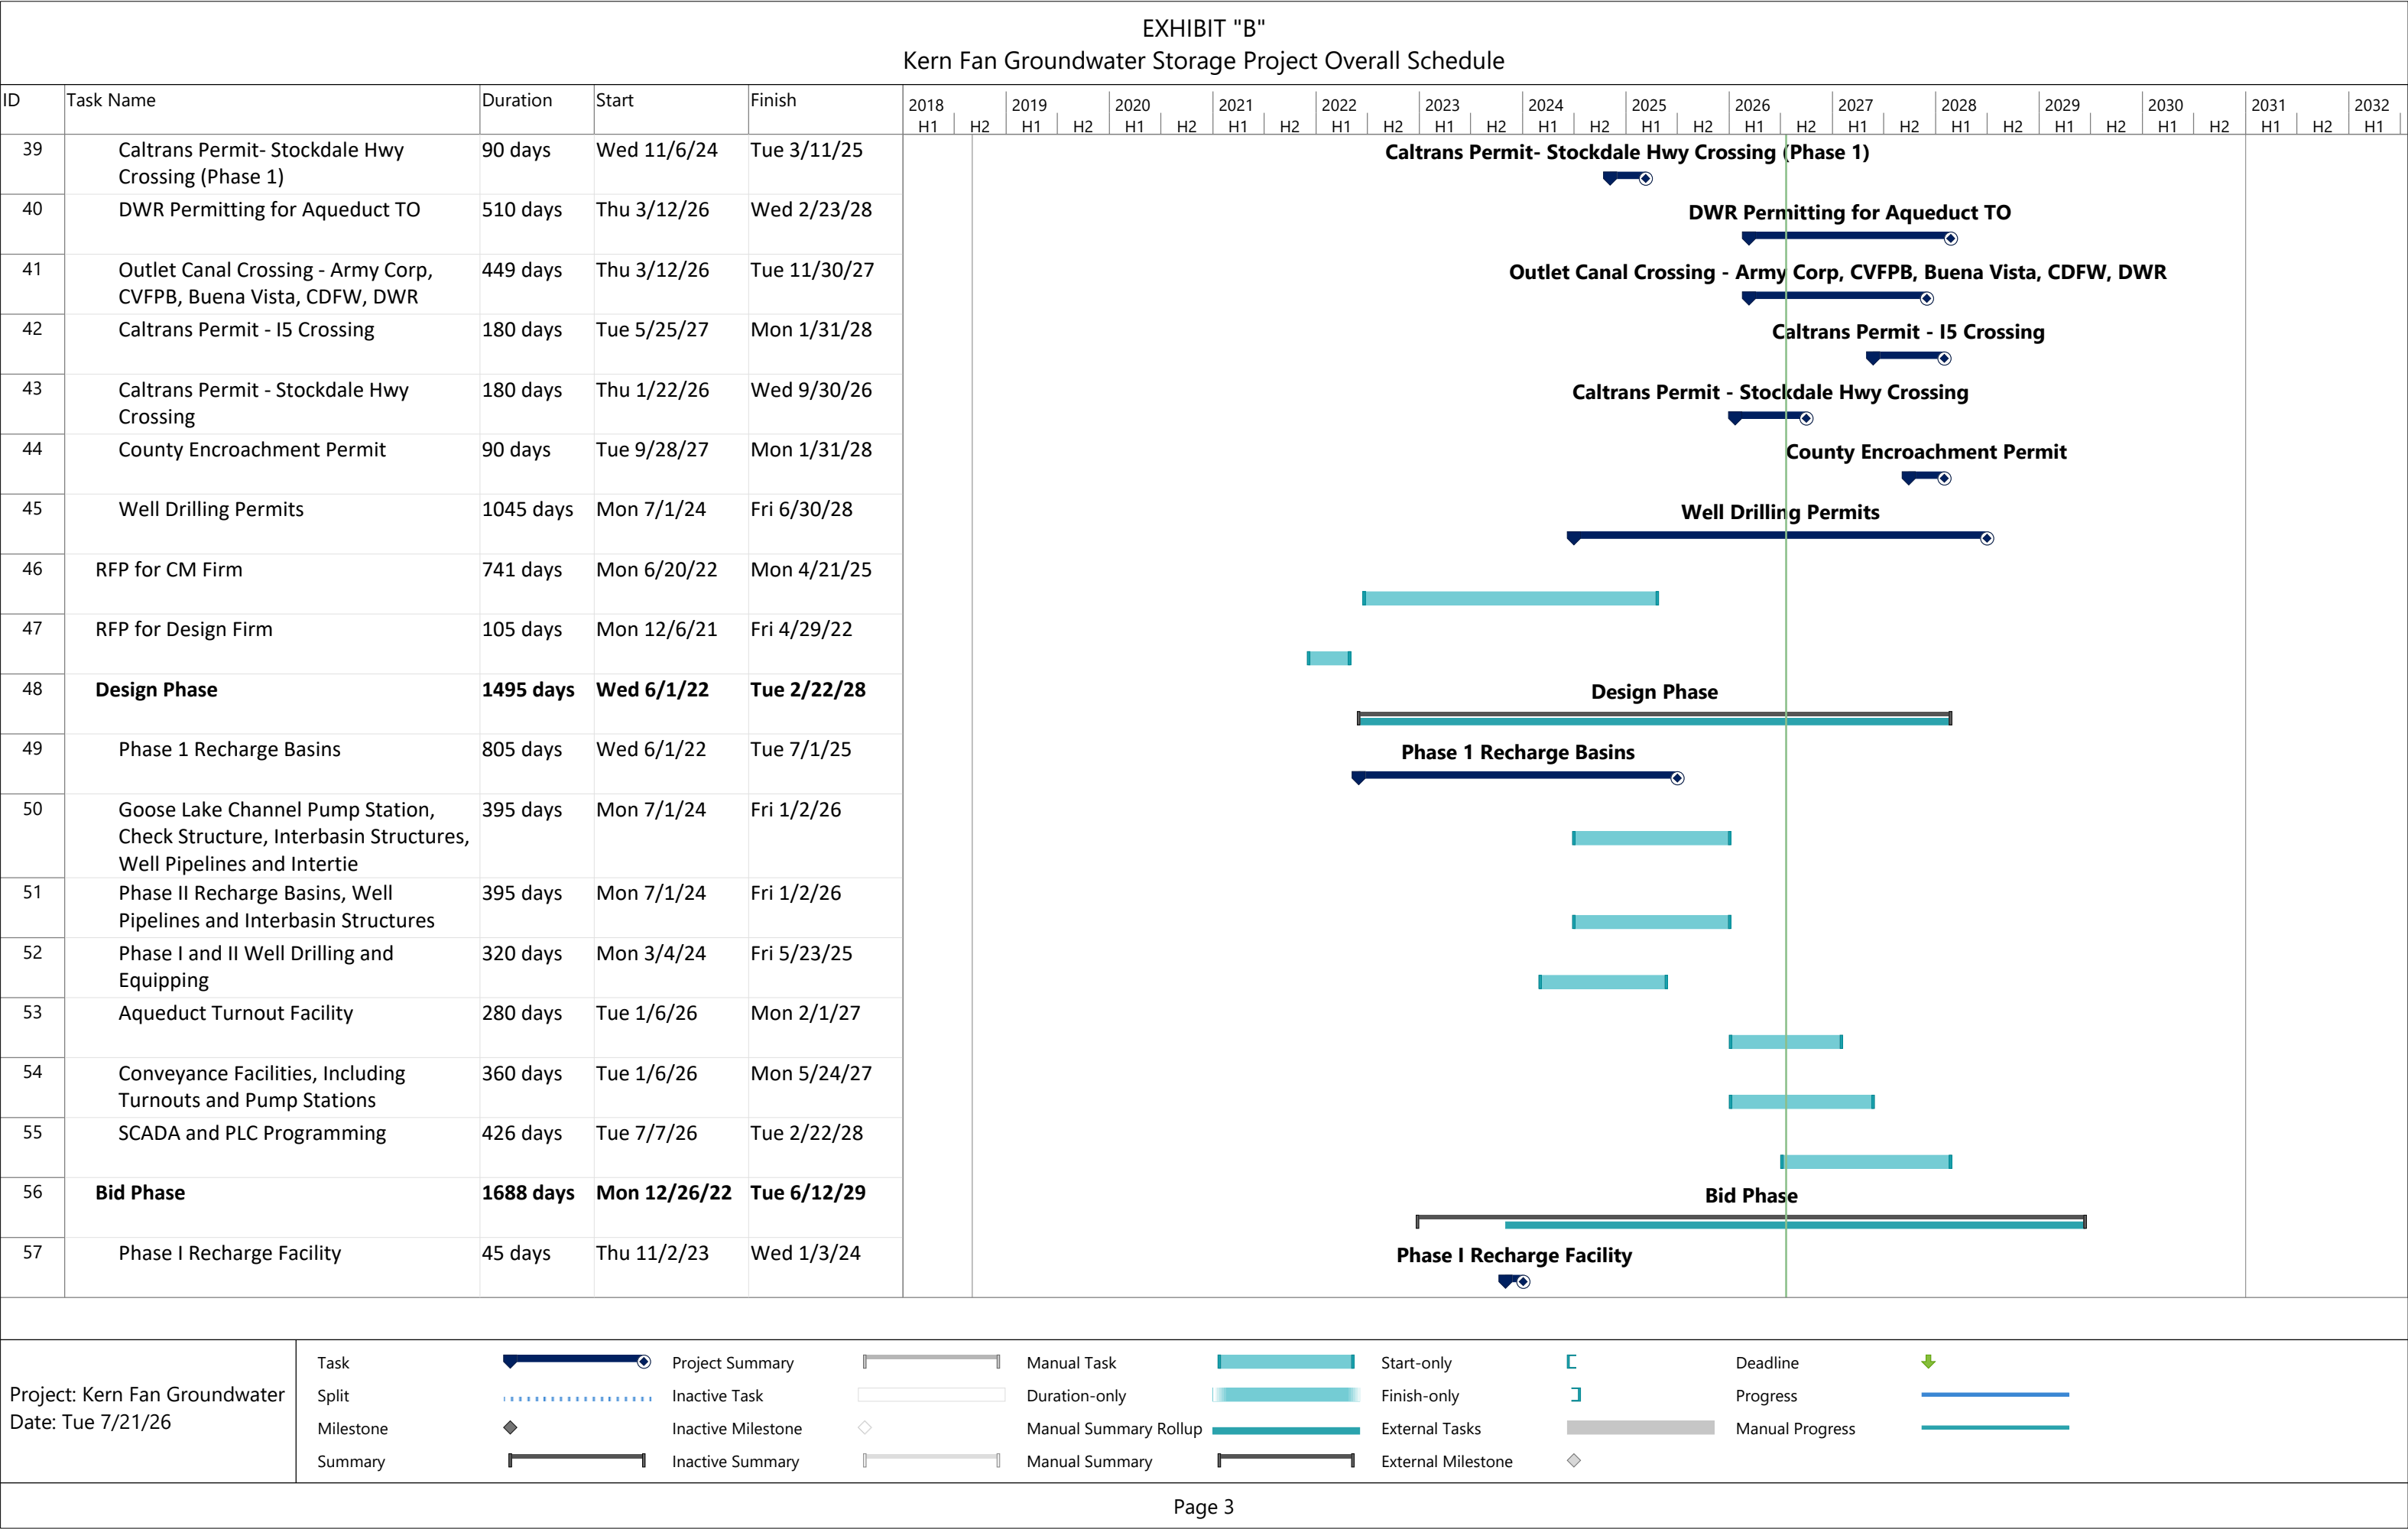

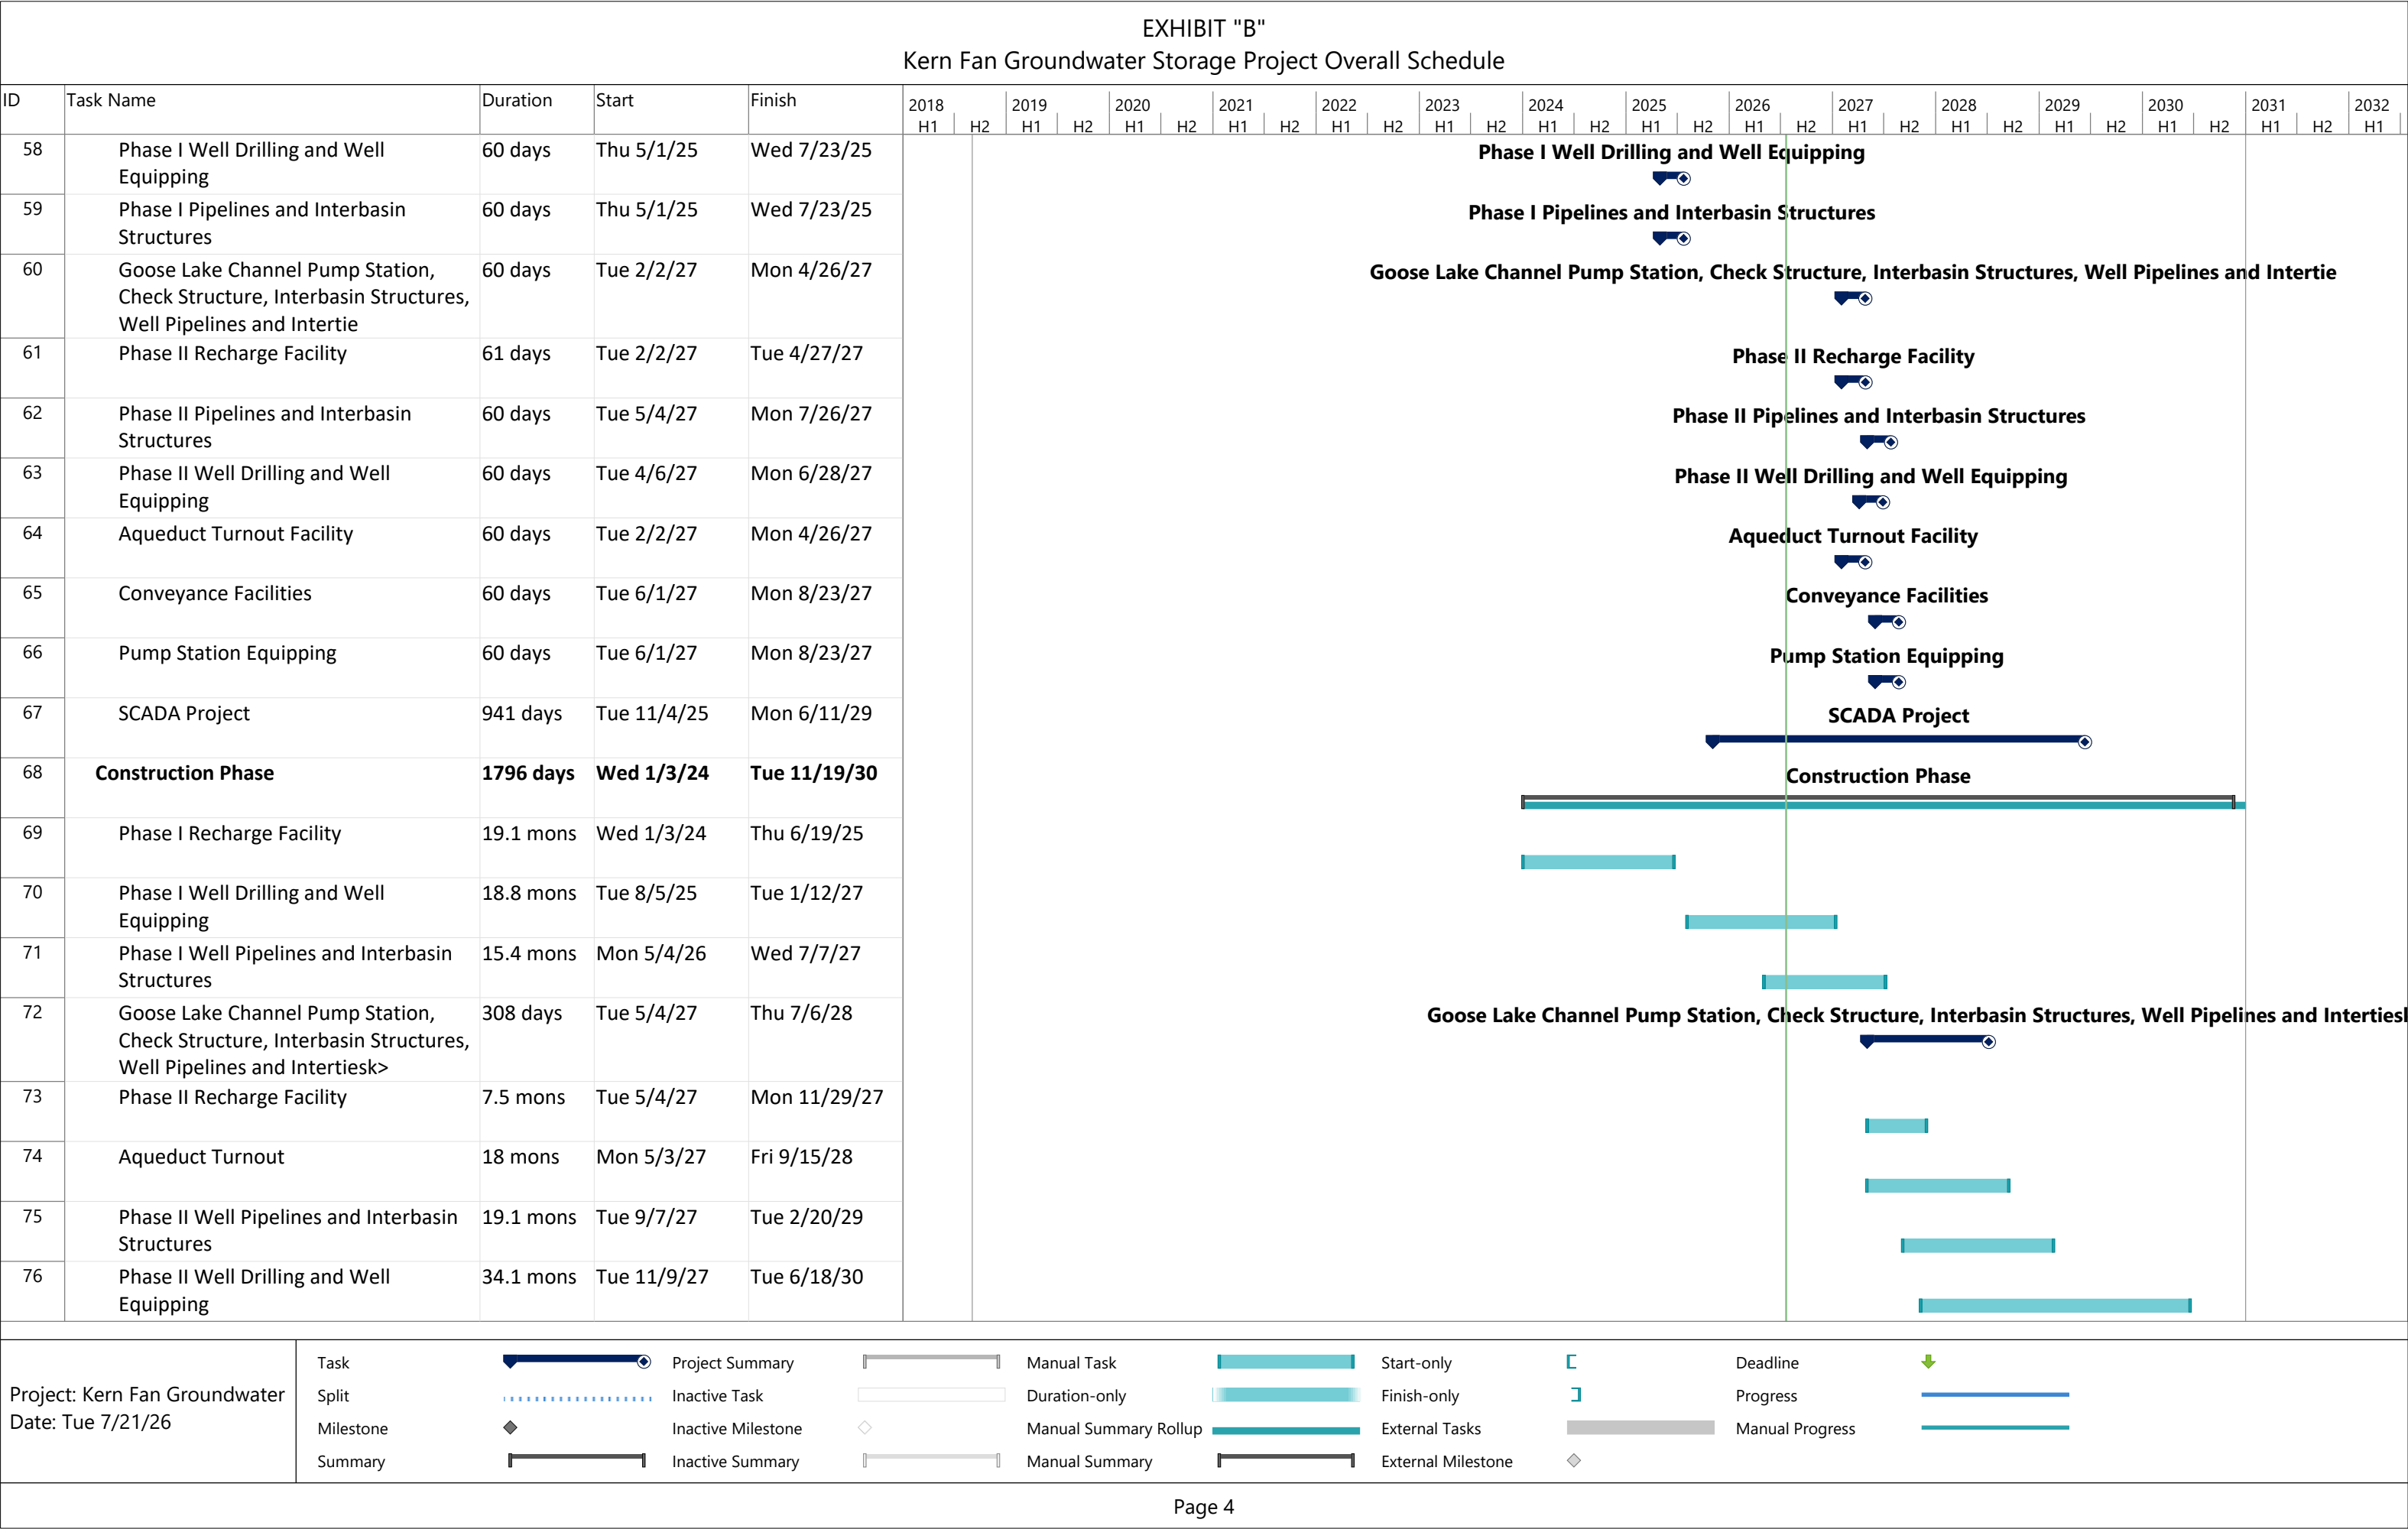




Exhibit "C"

All Required Federal, State, and Local Approvals, Certifications, and Agreements

	Start		Required to Initiate Phase 2/ Deliver Public Benefits to the Delta	
Permits		Complete		Notes
Caltrans Permit - Enos Lane Crossing Phase 1	Jul-24	Nov-24	N/A	Permit Issued
Caltrans Permit - Stockdale Hwy Crossing Phase 1	Jul-24	Nov-24	N/A	Permit Issued
Petition for Instream Flow Dedication (1707)	Oct-24	Oct-25	N/A	As of April 2025 per David Okita, State Board has indicated it will not be required.
Outlet Canal Crossing - Permits and Approvals:	Mar-26	Nov-27	Yes	
<i>Army Corps of Engineers</i>				Section 404
<i>Regional Water Quality Control Board</i>				Section 401
<i>California Dept of Fish and Wildlife</i>				Section 1601 Lake and Streambed Alteration Agreement
<i>DWR Turnout</i>				Encroachment Permit/Right of Entry
<i>State Parks - Tule Elk Preserve</i>				Encroachment Permit - need depends on final alignment of conveyance
<i>Central Valley Flood Protection Board</i>				Encroachment Permit
Caltrans Permit I-5 Crossing	May-27	Jan-28	Yes	
Caltrans Permit - Stockdale Hwy Crossing	May-27	Sep-26	Yes	
Incidental Take Permit - CDFW	Nov-26	Nov-27	Yes	
Kern County Environmental Health Dept - Well Drilling Permits	Jul-24	Jun-28	No	Wells are phased in. Permits can be secured earlier.
Right of Way and Easements	Start	Complete	Required to Initiate Phase 2/Deliver Public Benefits to the Delta	Notes
Executed Right of Way and Easements for Conveyance	Mar-22	Sep-27	Yes	Requirements for easements and right of way will depend on property acquisition locations and final canal alignment
California Dept of Fish and Wildlife				Approval of conveyance easement across Kern Water Bank Habitat Conservation Plan (HCP) area (could be part of ITP approval above)
Kern Water Bank Authority				Conveyance easement across Kern Water Bank property
Kern County Water Agency				Cross Valley Canal easement and/or crossing. Approval for Aqueduct turnout.
Agreements	Start	Complete	Required to Initiate Phase 2/Deliver Public Benefits to the Delta	Notes
Article 21 Agreement between DRWD/IRWD/KCWA/DWR	Jul-26	Dec-27	Yes	Approval of a change in Point of Delivery of a portion of DRWD SWP supplies (consent by Metropolitan Water District of Southern California)
Pulse Flow Exchange Agreement between DWR/KCWA/DRWD/GBJPA	Jul-26	Dec-27	Yes	
Cross Valley Canal (CVC) Operations Agreement with CVC Participants	Jul-26	Dec-27	Yes	
DWR/KCWA Turnout Agreement	Jul-26	Dec-27	Yes	
CDFW - Public Benefits Agreement	Sep-25	Dec-27	Yes	
